		<h1>Job Summary</h1>		Ticket Number TN# BCO-1812-0002		Ticket Date 12/1/2018	
COUNTY		COMPANY		API Number			
Weld		HIGHPOINT OPERATING		05-123-48499			
WELL NAME		RIG		JOB TYPE			
Wetco 4-63-5-5649C		Cartel 7		Surface Casing			
SURFACE WELL LOCATION		CJES Field Supervisor		CUSTOMER REP			
40.339865 104.449854		Derek Scott		Dustin Davis			
EMPLOYEES							
WELL PROFILE							
Max Treating Pressure (psi):				Bottom Hole Static Temperature (°F):			
Bottom Hole Circulating Temperature (°F):				Well Type:			
Open Hole							
1	Size (in)	TMD From (ft)	TMD to (ft)	TVD From (Ft)	TVD to (Ft)		
	13.5	0	841				
2	Size (in)	TMD From (ft)	TMD to (ft)	TVD From (Ft)	TVD to (Ft)		
Casing/Tubing/Drill Pipe							
Type	Size (in)	Weight (lb/ft)	Grade	TMD From (ft)	TMD to (ft)	TVD From (Ft)	TVD to (Ft)
Surface	9.625	36	J-55	0	841		
Type	Size (in)	Weight (lb/ft)	Grade	TMD From (ft)	TMD to (ft)	TVD From (Ft)	TVD to (Ft)
Type	Size (in)	Weight (lb/ft)	Grade	TMD From (ft)	TMD to (ft)	TVD From (Ft)	TVD to (Ft)
CEMENT DATA							
Stage 1:		From Depth (ft):	0	To Depth (ft):	841		
Type: Lead		Volume (sacks):	260	Volume (bbls):	89.3		
Cement & Additives:		Density (ppg)	13	Yield (ft³/sk)	1.93	Water Req.	
100% CSC +0.25pps Poly Flake						10.54	
Stage 2:		From Depth (ft):		To Depth (ft):			
Type:		Volume (sacks):		Volume (bbls):			
Cement & Additives:		Density (ppg)		Yield (ft³/sk)		Water Req.	
Stage 3:		From Depth (ft):		To Depth (ft):			
Type:		Volume (sacks):		Volume (bbls):			
Cement & Additives:		Density (ppg)		Yield (ft³/sk)		Water Req.	
Stage 4:		From Depth (ft):		To Depth (ft):			
Type:		Volume (sacks):		Volume (bbls):			
Cement & Additives:		Density (ppg)		Yield (ft³/sk)		Water Req.	
SUMMARY							
Stage 2							
Preflushes:	23 bbls of	Fresh Water	Calculated Displacement (bbl):	61.6			
	10 bbls of	Dye	Actual Displacement (bbl):	61.6			
	bbls of						
Total Preflush/Spacer Volume (bbl):	33	Plug Bump (Y/N):	Yes	Bump Pressure (psi):	780		
Total Slurry Volume (bbl):	89.3	Lost Returns (Y/N):	No	(if Y, when)			
Total Fluid Pumped	183.9						
Returns to Surface:	Cement		bbls				
Job Notes (fluids pumped / procedures / tools / etc.):							
Job went well. We bumped on time and we had circulation the whole time.							
Thank You For Using							
CJES O-TEX Cementing							
Customer Representative Signature: _____							


Cement Job Log

[illegible]




Client	High Point	Client Rep	Dustin Davis	Supervisor	Derek Scott
Ticket No.	18120002	Well Name	Wetco 4-63-5-5649C	Unit No.	445067
Location	NWSW 4-4N-63W	Job Type	Surface Casing	Service District	Brighton, CO
Comments	260sx CSC @ 13.0ppg 1.93yield			Job Date	12/1/2018


Unit 445067 Rate Total

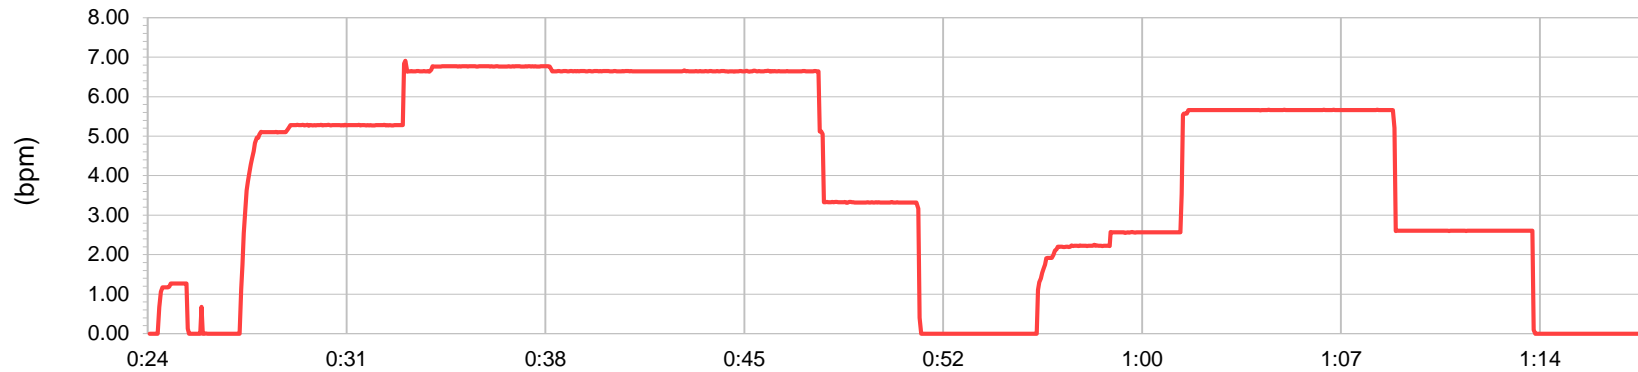


Unit 445067 Pump Pressure

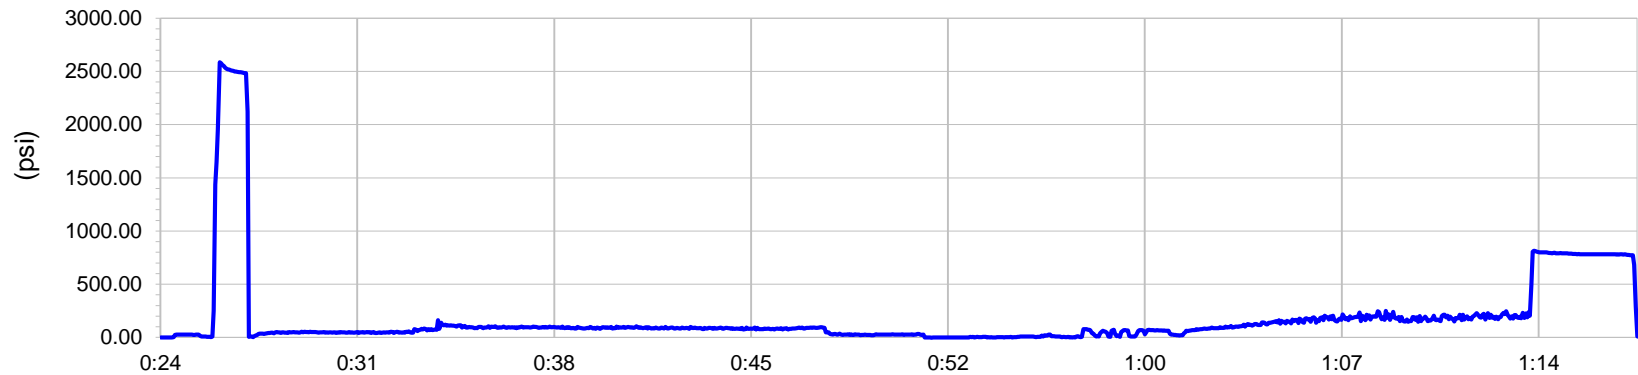

Unit 445067 Density

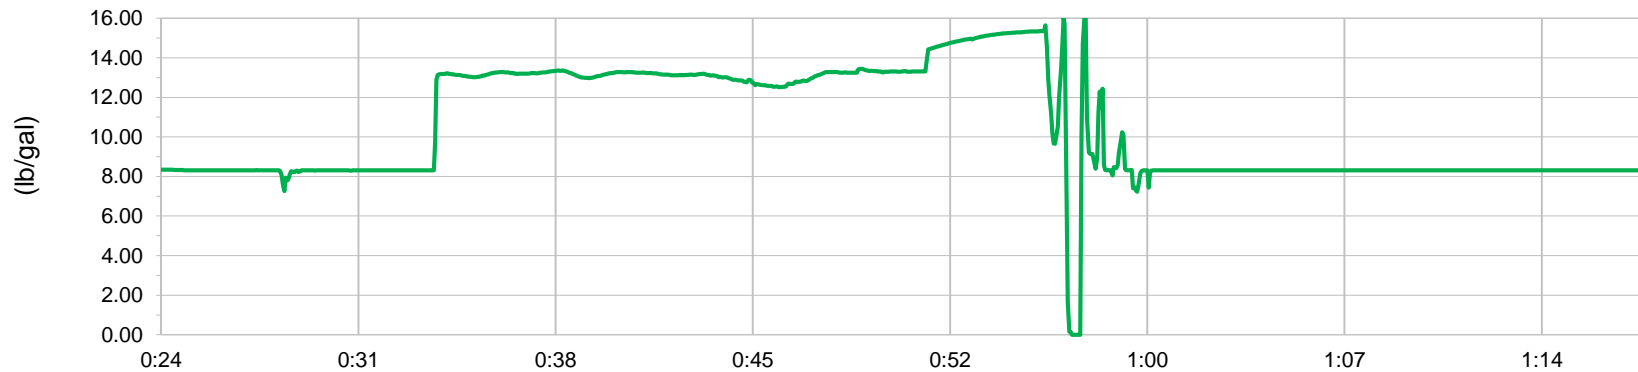



TICKET	BCO-1812-0002
DATE	12/1/2018
CREW INFORMATION	
SUPERVISOR	Derek Scott
PUMP UNIT	445067
NUMBERS	
ARRIVAL (D&T)	11/30/18 9:15 PM
DEPARTURE (D&T)	12/1/18 1:50 AM

[illegible][illegible]

Customer Name Printed _____

Customer Signature _____

Date Signed _____
