



# YETTER WELL SERVICE, INC.

P.O. Box 1808 • Sterling, Colorado 80751-7808

Phone (970) 522-2885

Date 1-21-13

COMPANY Schneider Oil & Gas

LEASE Patterson

WELL NO. 1

RIG 9

COUNTY Morgan

Work Ordered By: Jeff Schneider Job Description: Plug well

			HOURS	TOTAL
Road to location, rig up rig, rig up for rods, unhang well, unseat pump, lay down polish rod, subs, pull 1 triple to derrick, paraffin rips out wiping rubber, pick up polish rod, cap off well, shut down for Hot oiler in morning.			3	
RODS				
PUMP				
SUBS				
TUBING				
SUBS				
OTHER				
Remarks:				
FURNISHED 1 rod wiping rubber				\$ 9.00
UNIT CHARGE Justin K.			3	765.00
John d.			3	
Chris H.			3	
TAX				26
TOTAL				\$ 774.26



# YETTER WELL SERVICE, INC.

P.O. Box 1808 • Sterling, Colorado 80751-7808

Phone (970) 522-2885


Date 1-22-13

COMPANY Schneider Oil & Gas LEASE Patterson WELL NO. 1

RIG 9 COUNTY Morgan

Work Ordered By: Jeff S. Job Description:

			HOURS	TOTAL
Travel to location, warm rig, rig up for rods, unspool well, rig up Hot oiler, pump 40 BBL of Hot water down backside and tubing, rig down Hot oiler, lay down polish rod, pull rods to derrick, lay down pump, rig up for tubing, unlead tubing, unset anchor, pull/tally tubing to derrick, run model R procter on tubing, set procter, end off well, shut down for night.			11	
RODS				
PUMP				
SUBS				
TUBING				
SUBS				
OTHER				
Remarks:				
FURNISHED				
75 BBL Flat Tank				\$ 50.00
2 3/8 wiping rubber				29.00
UNIT CHARGE				
Justin E.			11	2805.00
John D.			11	
Chris H.			11	
2.9% TAX				.84
TOTAL				\$ 2841.84

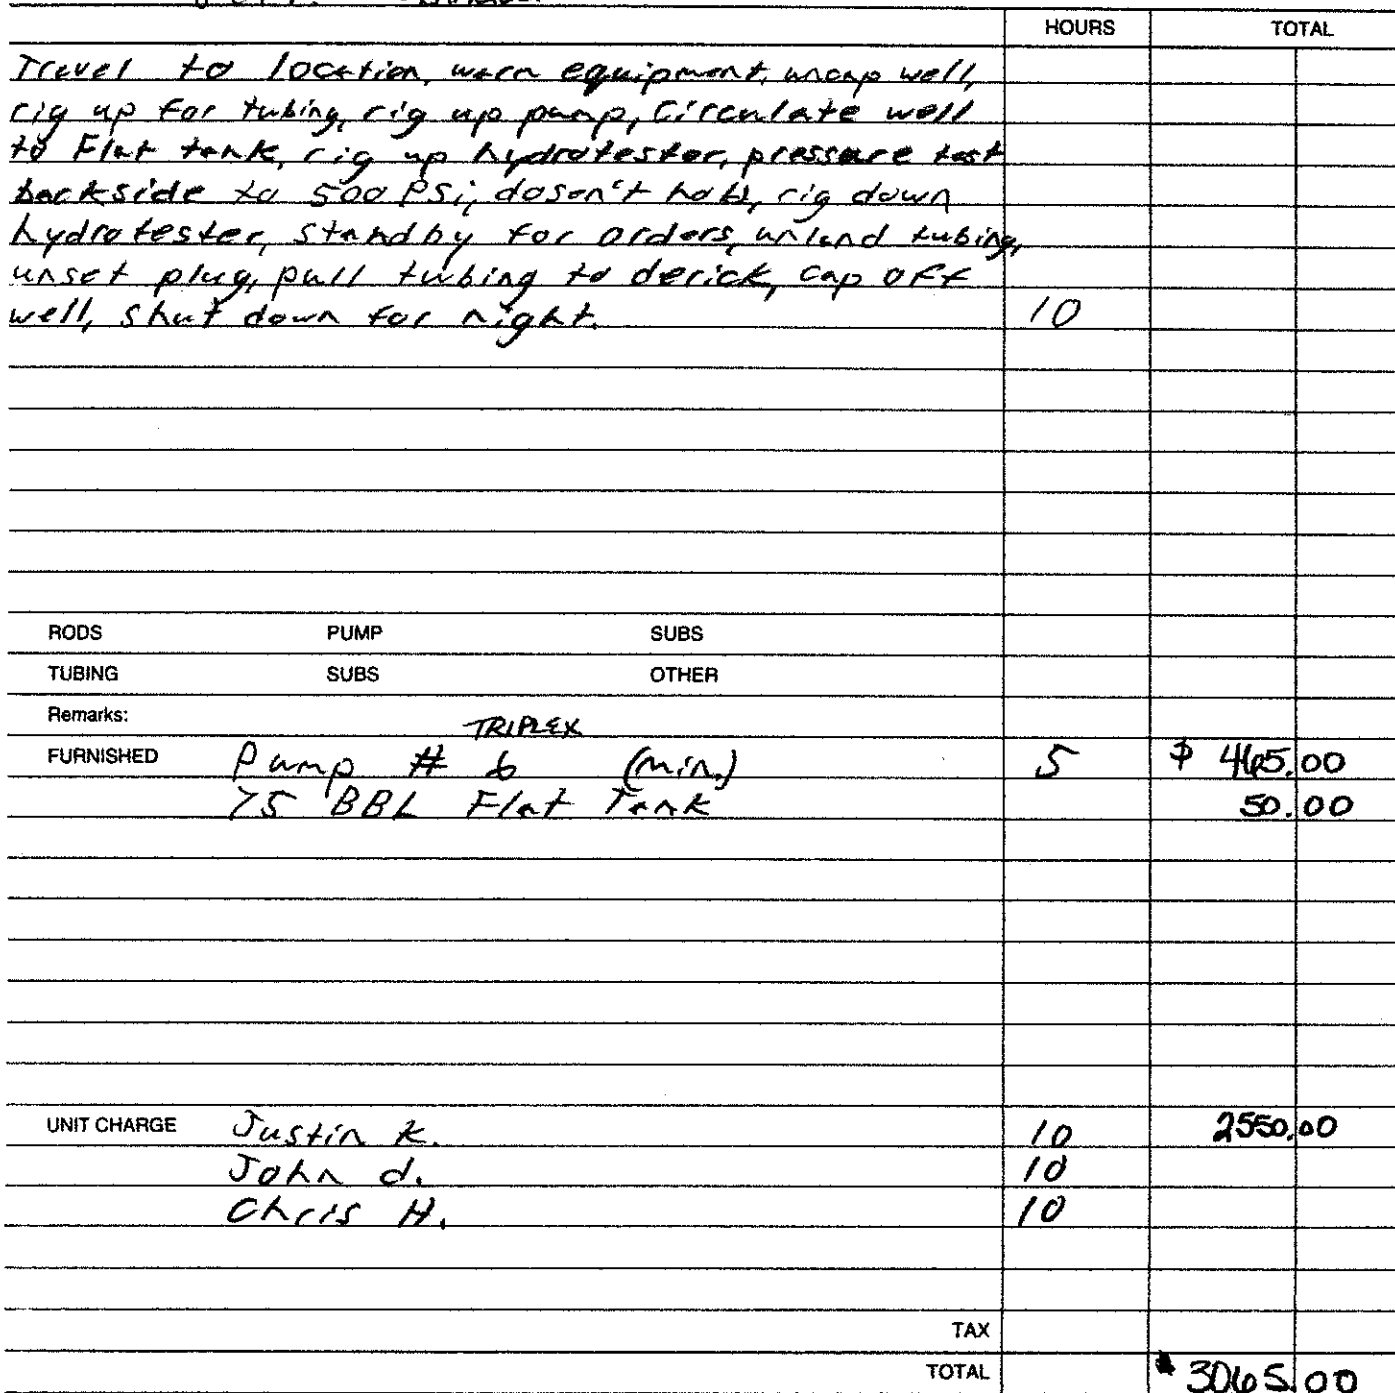



# YETTER WELL SERVICE, INC.

P.O. Box 1808 • Sterling, Colorado 80751-7808

Phone (970) 522-2885

Date 1-25-13

COMPANY Schneider Oil and Gas LEASE Patterson WELL NO. 1  
RIG 9 COUNTY Morgan

Work Ordered By: Jeff S. Job Description:

	HOURS	TOTAL
Travel to location, warm rig, uncrap well, rig up J.W. wireline, set plug at 5,975', shoot 3 holes in casing at 5,280', set retainer at 5,230', rig down J.W. run in 2 3/8 string-in tool on tubing out of derrick, string into retainer, rig up pump and cement mixer, pump 30 sacks of cement, string out of retainer, pull 50 strands to derrick, lay down rest of tubing on trailer flat, take off wellhead, unload casing, work casing to 70,000 LBS, reload casing, cap off well, shut down for weekend.	11	

RODS	PUMP	SUBS
TUBING	SUBS	OTHER

Remarks:		
FURNISHED		
4 1/2 Elevators		\$ 110.00
25 BBL Flat Tank		50.00
Pump #6	2	186.00
Cement Mixer	2	132.00
2 3/8 Stripping Rubber		137.00
30 Sacks Cement (Included in total.)		422.00
1 sack calcium chloride		14.85

UNIT CHARGE		
Justin K.	11	2805.00
John d.	11	
Chris H.	11	

2.9% TAX	151.85	4.40
TOTAL		3439.25



# YETTER WELL SERVICE, INC.

P.O. Box 1808 • Sterling, Colorado 80751-7808

Phone (970) 522-2885

Date 1-24-13

COMPANY Schneider Oil and Gas

LEASE Patterson

WELL NO. 1

RIG 9

COUNTY Morgan

Work Ordered By: JEFF S.

Job Description:

			HOURS	TOTAL
Travel to location, warm rig, rig up for tubing, wrap well, run tubing out of derrick half way, rig up swab bar, swab 4 runs down flowline, stand back swab bar, run the rest of tubing out of derrick, rig up for rods, run rods out of derrick, lay down rods on trailer, rig up for tubing, pull 84 stands to derrick, lay down rest of pipe on trailer, cap off well, shut down for night.			12	
RODS	PUMP	SUBS		
TUBING	SUBS	OTHER		
Remarks:				
FURNISHED	25 BBL Flat Tank			\$ 50.00
	2 2 <sup>3</sup> / <sub>8</sub> wire swab cups @ *21.75			43.50
	1 Gallon Bakeread			52.00
UNIT CHARGE				
	Jaspin K.		12	3060.00
	John d.		12	
	Chris H.		12	
2.9% TAX			95.50	2.77
TOTAL				*3208.27



# YETTER WELL SERVICE, INC.

P.O. Box 1808 • Sterling, Colorado 80751-7808

Phone (970) 522-2885

Date 1-28-13

COMPANY Schneider Oil and Gas LEASE Patterson WELL NO. 1

RIG 9 COUNTY Morgan

Work Ordered By: Jeff S. Job Description:

		HOURS	TOTAL
Travel to location, warm rig, uncap well, rig up for casing, rig up J.W. wireline, balance casing, cut off casing at 4,394', rig down J.W., lay down 108 joints of casing down, holes in casing in J.W. to and to 64', rig up for tubing, rig up well head, run 14 stands out of derrick, rig up stripping rubber, cap off well, shut down for night.		9 1/2	
RODS	PUMP	SUBS	
TUBING	SUBS	OTHER	
Remarks: Pump 12 BBLs down casing to kill well			
FURNISHED	4 1/2" Elevators		\$ 110.00
	25 bbl Flat Tank		50.00
	Cement bleeding Unit	1	700.00
	1-Ton csg tool bucket	4	272.00
	4 1/2" csg tools 4,400' pipe recovered @ 15¢/ft.		660.00
	EXTRA LABOR	9	405.00
	4 1/2" csg wiping rubber		63.75
	Tool Pusher 1/2 day		250.00
UNIT CHARGE	Justin R.	9 1/2	242.50
	John D.	9 1/2	
	Chris H.	9 1/2	
		TAX	63.75
		TOTAL	1.85
			\$4935.10



# YETTER WELL SERVICE, INC.

P.O. Box 1808 • Sterling, Colorado 80751-7808

Phone (970) 522-2885

Date 1-29-13

COMPANY Schneider Energy

LEASE Patterson

WELL NO. 1


RIG 9

COUNTY Morgan


Work Ordered By: Jeff S.

Job Description: Plug

		HOURS	TOTAL
Travel to location, warm equipment, uncap well, rig up for tubing, run 139 joints in hole, rig up pump and cement mixer, pump 30 sacks at casing stub. Lay down all tubing but 11 joints pump well pill, pump 50 sacks of cement, lay down rest of pipe, let cement set up, 4 hours TAGGED Cement plug at 130', run in 2 joints in hole, top off surface with 33 sacks, lockout pump and cement mixer, rig down rig, leave matted up, shut down for night.		10	
RODS <u>7 1/8 168 3/4</u>	PUMP <u>—</u>		
TUBING <u>19 1/2 3/8</u>	SUBS <u>NONE</u>		
OTHER <u>5' below casing</u>			
Remarks:			
FURNISHED	75 BBL Flat Tank		\$ 50.00
	90 BBL Flat Tank		50.00
	Pump # 6	5	465.00
	Cement Mixer	5	330.00
	2 3/8 wiping rubber		29.00
	143 sacks for job (8 bags used) CEMENT		2002.00
UNIT CHARGE	Justin K.	10	2550.00
	John d.	10	
	Chris H.	10	
TAX		2031.00	* 58.90
TOTAL			* 5534.90

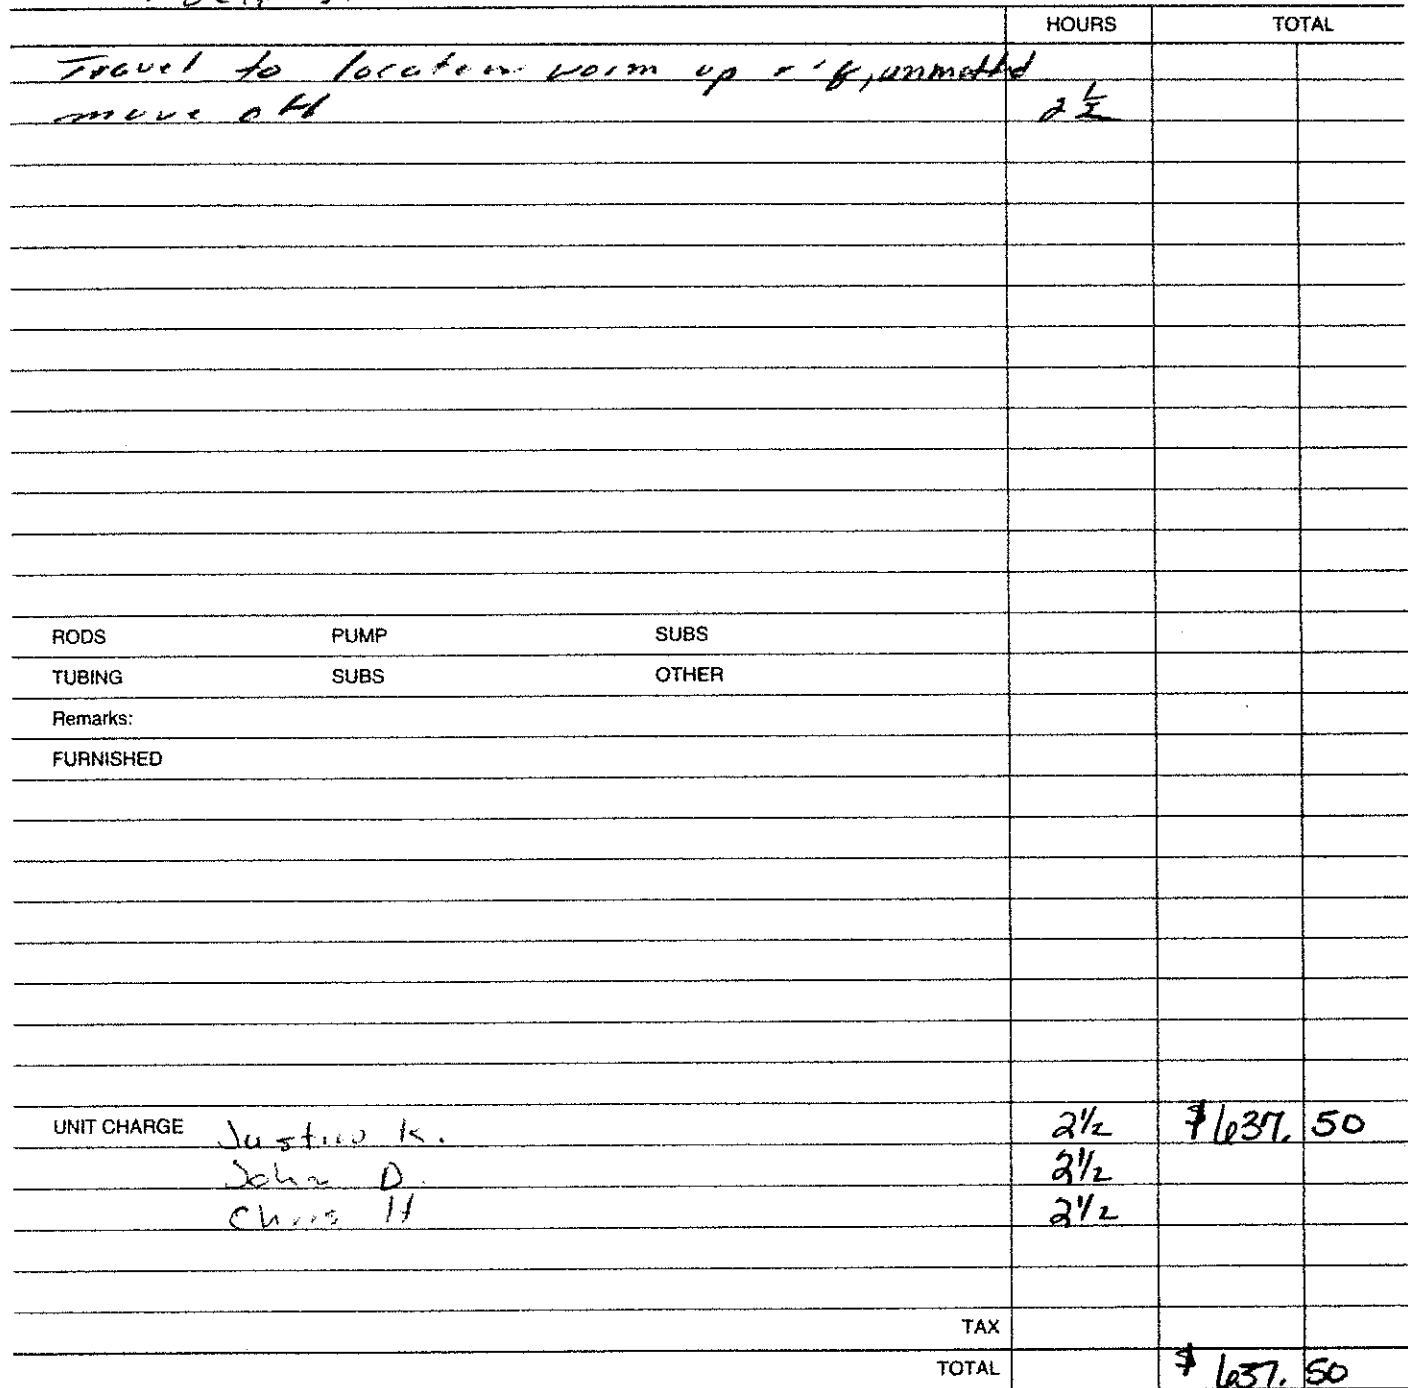



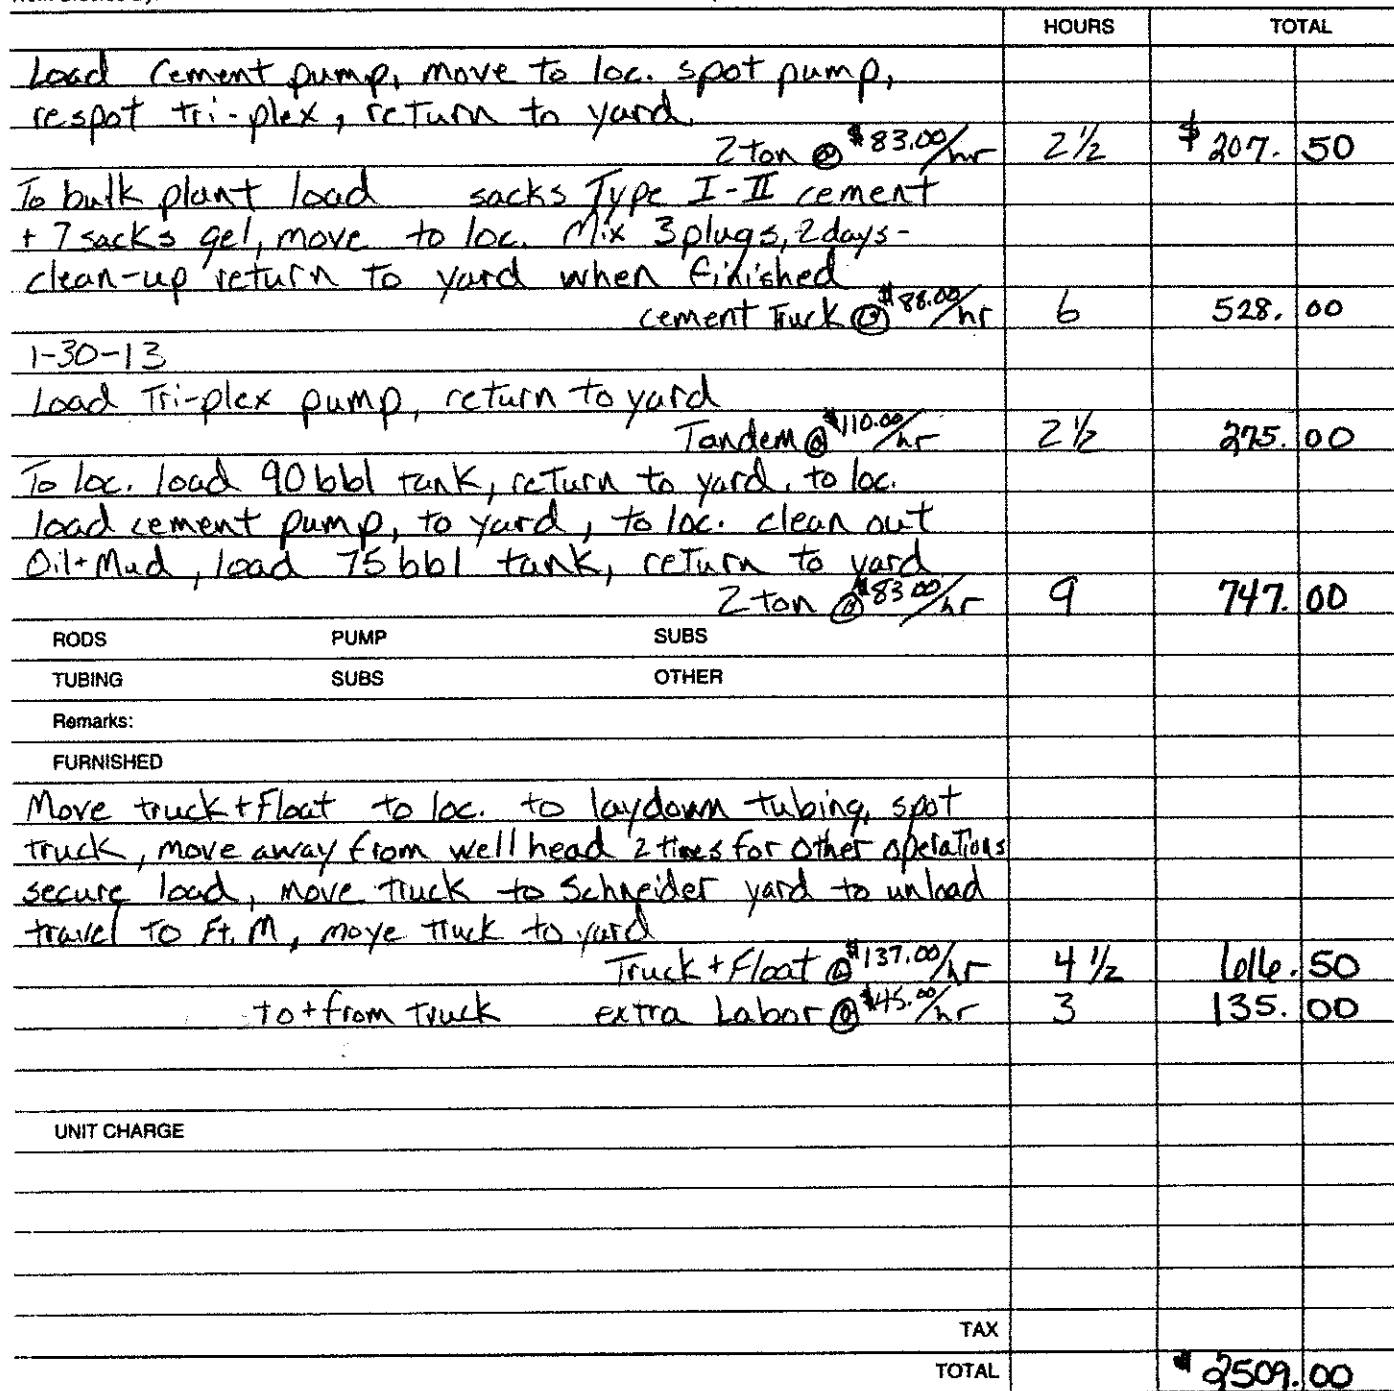

**Sterling Ready Mix**

P.O. Box 1908  
Sterling, CO 80751  
Phone: (970) 522-1263

Ticket No.:

**CUSTOMER****12249**

Date: 1/24/2013 Time: 10:52:00AM

Carrier: 103

Sterling Redi-Mix

Location: **Sterling Ready Mix**

Vehicle:

Customer: 10340 Yetter Well Service

Order: 5701134 Cement at Plant

P.O.:

<u>Product</u>	<u>Description</u>	<u>Qty</u>	<u>Unit</u>	<u>Unit Price</u>	<u>Amount</u>
35101196	Cement Type I-II	6.58	Ton		

Received:



Patterson #1

Subtotal:
Freight:
Tax:
Total Due:

COPY 3 - CUSTOMER COPY

Weighmaster: Cecil Souders
